

**City of Newton**Ruthanne Fuller, Mayor









### **AGENDA**

- **SCHEDULE UPDATE**
- **PROGRESS PHOTOS**
- **CONTACTS**











#### **SCHEDULE UPDATE**

cornice nearly complete, **Exterior Envelope** 

ceiling below gym ongoing

**Interior Finishes** October 2025

**Final Sitework** October 2025

**FF&E Deliveries** November 2025

**Substantial Completion** Fall 2025










### **PHOTOGRAPHS**



Roof Decking Installed, Railings Ongoing

> Final grading Ongoing at Front of Building



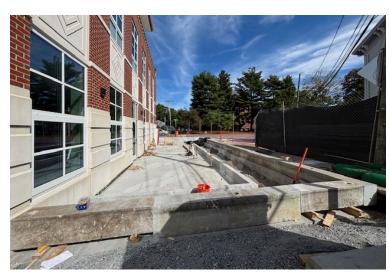

Exterior Patio Curbing Installed



Entry Canopy Ongoing







**COOPER CENTER FOR ACTIVE LIVING COMMUNITY UPDATE** 



Exterior Panels and Cornice Ongoing




Railings in **Egress Stairs** Installed



**COOPER CENTER FOR ACTIVE LIVING COMMUNITY UPDATE** 

**Binder Coat Paving** Complete, Lights & EV Charger Install Ongoing












# **PHOTOGRAPHS**



Gym Ceiling Work Complete, Flooring to Begin



Corridor **Painting** Complete

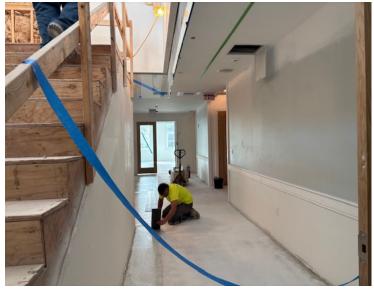

**COOPER CENTER FOR ACTIVE LIVING COMMUNITY UPDATE** 

Flooring Under Way at

Flooring Ongoing at Main Corridor







Restroom Corridor



## **Q&A**

#### **Project Information**



- www.facebook.com/BuildingsNewtonMA/
- www.instagram.com/newtonmapbd/

#### **Further Information**

Tom Rooney, City of Newton Project Manager Tom Murphy, NV5 Project Director trooney@newtonma.gov thomas.murphy@nv5.com







